

RESOLUTION NO. 2011-232

Adopted by the Sacramento City Council

April 21, 2011

WEST EL CAMINO AVENUE AND INTERSTATE 80 SIGNALIZATION PROJECT (S15084800) APPROVING CHANGE ORDER NO. 3 WITH TEICHERT CONSTRUCTION IN THE AMOUNT OF \$86,929

BACKGROUND

- A. The West El Camino Avenue and Interstate 80 Signalization Project (S15084800) will improve traffic circulation and safety, relieve congestion on the offramps and improve bicycle and pedestrian movement. The improvements include installing traffic signals at the off ramps, street lights, sidewalks, a raised median, pavement widening and rehabilitation, new striping and signage and two neighborhood monument signs.
- B. The project was advertised and bids were received on May 24, 2010. Teichert Construction was awarded the construction contract by City Council on June 22, 2010. The project is under construction and is expected to be completed in June 2011.
- C. Change Order No. 1 in the amount of \$48,730 compensated the contractor for various items which include the shared cost of flagging to maintain public safety, boring for a new electrical conduit that was found in bad condition when uncovered during the project, placing geogrid for the unsuitable sub base and extra grading to improve the drainage on the eastbound offramp. This change order also included the modifications to the community signs to better fit the requested community logo.
- D. Change Order No. 2 in the amount of \$84,330 compensated the contractor for improving safety and adding additional staging phases to maintain the roadway open during construction and accommodate access to the large trucks entering the 49er Truck Stop for each phase. Imported borrow dirt was also added to provide better drainage and aesthetics to the offramps. This change order also compensated the contractor for installing temporary erosion control blankets, extended inlet protection and hydroseeding to keep the rain from eroding the newly imported borrow dirt keeping the roadway clear of dirt erosion and maintaining the quality of the water runoff required by the Storm Water Pollution Prevention Program (SWPPP).
- E. Change Order No. 3 in the amount of \$86,929 will compensate Teichert

Construction for extra work performed to winterize the project. Due to the cold temperatures, the required night work will be completed in May or June. The project had increased quantity in fiber rolls, hydroseeding, site monitoring and testing throughout the winter to conform to the new rules and requirement of the SWPPP regulated by the California Regional Water Quality Board that began on July 1, 2010 after the project was awarded. This change order also includes the shared cost of flaggers and staging costs needed to direct the public through the construction site safely. This project is also in the jurisdiction of Caltrans and the County and both agencies made construction changes which required the City to modify the design and increase the quantities of the sidewalk, curb and gutter and 49er Truck Stop driveway.

BASED ON THE FACTS SET FORTH IN THE BACKGROUND, THE CITY COUNCIL RESOLVES AS FOLLOWS:

- Section 1. The City Manager is authorized to execute Change Order No. 3 with Teichert Construction in the amount not to exceed \$86,929 for the West El Camino Avenue and Interstate 80 Signalization Project (S15084800).
- Section 2. The City Manager's change order authority is reset.

Table of Contents

Exhibit A – Map of West El Camino and Interstate 80 Location (S15084800)

Adopted by the City of Sacramento City Council on April 21, 2011 by the following vote:

Ayes: Councilmembers Ashby, Cohn, D Fong, R Fong, McCarty, Pannell, Schenirer.

Noes: None.

Abstain: None.

Absent: Councilmembers Sheedy, and Mayor Johnson

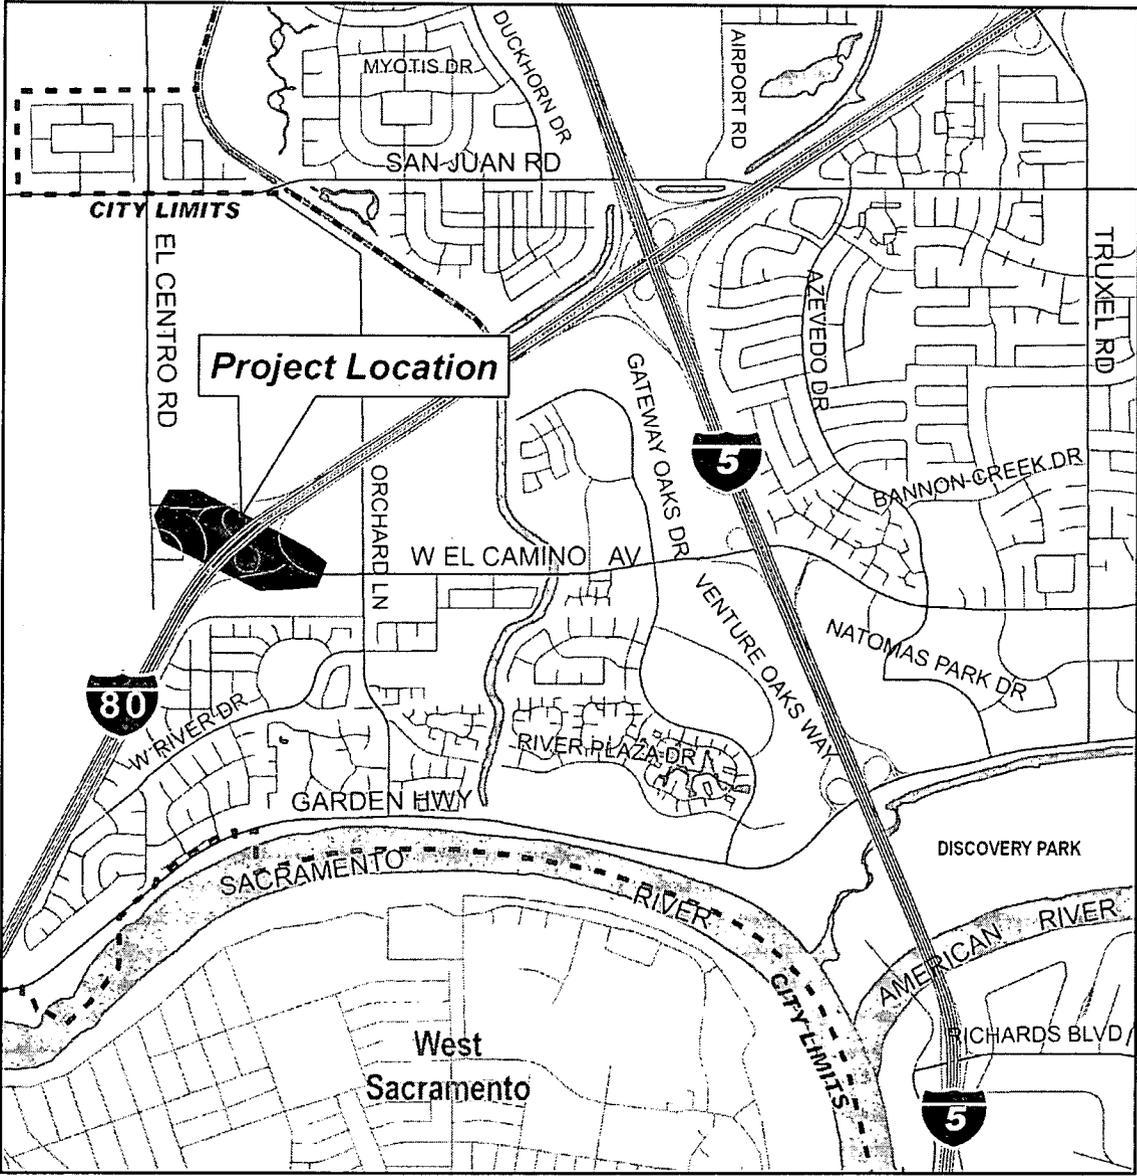

Bonnie Pannell, Vice-Mayor

Attest:


for Shirley Concolino, City Clerk

EXHIBIT A

Location Map for
West El Camino / Interstate 80 Interchange Signalization
(S15084800)



Department of
TRANSPORTATION
City of Sacramento

Map Contact: S. Tobin
Map Date: April, 2009

