



City of Sacramento City Council

6

915 I Street, Sacramento, CA, 95814
www.CityofSacramento.org

Meeting Date: 8/30/2011

Report Type: Consent

Title: Contract: Southside Park Picnic Area Renovation Project (L19162104)

Report ID: 2011-00754

Location: 2115 6th Street ,District 4

Recommendation: Adopt a Resolution: 1) approving the contract plans and specifications for the project; 2) appropriating \$24,000 of Park Development Impact Fees (PIF), Fund 3204, to the project 3) awarding the contract to RSC General & Engineering, Inc. for improvements in the park for an amount not to exceed \$196,186.37; and 4) authorizing the City Manager, or City Manager's designee, to execute the contract with RSC General & Engineering, Inc. for the project.

Contact: Tin-Wah Wong, Associate Landscape Architect, (916) 808-5540; J.P. Tindell, Park Planning & Development Manager, (916) 808-1955, Department of Parks and Recreation

Presenter: None

Department: Parks & Recreation Department

Division: Park Development Services

Dept ID: 19001121

Attachments:

-
- 1-Description/Analysis
 - 2-Background
 - 3-Location Map (Southside Park)
 - 4-Southside Park Picnic Area Improvements
 - 5-Resolution
 - 6-Exhibit A (Construction Contract)

City Attorney Review

Approved as to Form
Sheryl N. Patterson
8/23/2011 10:58:46 AM

City Treasurer Review

Prior Council Financial Policy Approval or
Outside City Treasurer Scope
Russell Fehr
8/16/2011 10:19:58 AM

Approvals/Acknowledgements

Department Director or Designee: Jim Combs - 8/22/2011 10:08:29 AM

Assistant City Manager: Cassandra Jennings - 8/23/2011 10:58:06 AM

Eileen Teichert, City Attorney

Shirley Concolino, City Clerk
William H. Edgar, Interim City Manager

Russell Fehr, City Treasurer

Description/Analysis

Issue: Southside Park is an existing 19.5-acre community park located at 2115 6th Street in the Central City Community Plan Area (PA1). On April 3, 2007, City Council adopted Resolution No. 2007-187 supporting the development of a Land and Water Conservation Fund (LWCF) Grant application for the renovation of the group picnic area at Southside Park, which was subsequently awarded. On May 19, 2009, City Council adopted Resolution 2009-301 establishing the Capital Improvement Program (CIP) for the Southside Park Picnic Area Renovation project (L19162104) and appropriating LWCF grant funds in the amount of \$142,985 and the required matching funds in the amount of \$142,985 from Park Development Impact Fees (PIF), Fund 3204, to the project.

Staff is now requesting City Council approval to award a contract for the Southside Park Picnic Area Renovation project. The formal bid process for the Southside Park Picnic Area Renovation project has been completed and RSC General & Engineering, Inc. has been selected as the lowest responsible and responsive bidder.

In order to award the contract as recommended, staff seeks approval to augment the existing project budget by appropriating \$24,000 of PIF, Fund 3204, to L19162104.

The group picnic area being renovated is located in the northwest corner of Southside Park at T and 6th Streets. A summary of the project history, a location map, and the proposed picnic area improvements are included as attachments to this report.

Policy Considerations: Sacramento City Code Chapter 3.60 identifies the general guidelines for completing contracts for public projects and procedures for bidding and issuing contracts over \$100,000.

Providing parks and recreation facilities is consistent with the City's strategic plan to enhance livability in Sacramento's neighborhoods by expanding park, recreation, and trail facilities throughout the City.

This is also part of the Park Development Process for park planning as stated in the *2005-2010 Parks and Recreation Master Plan*.

Utilizing Park Development Impact Fees, Fund 3204, to augment this budget is consistent with Sacramento City Code Section 18.44.160 as these funds will be "expended on park facilities within the planning area in which the development project paying the fee is located."

In accordance with Sacramento City Council Resolution No. 2010-346, RSC General & Engineering, Inc., is headquartered in the state of California. The proposed contract is

consistent with Resolution No. 2010-346 prohibiting the City from entering into any contract to purchase goods or services from any business or entity headquartered in Arizona.

Environmental Considerations:

California Environmental Quality Act (CEQA): The Environmental Services Manager has reviewed this project and determined that it is exempt from the provisions of CEQA pursuant to CEQA Guidelines (Title 14 Cal. Code Reg. § 15000 et seq.) sections 15302 and 15303 because it includes the replacement of existing structures with new structures located in the same site and have the same purpose and capacity as the structures being replaced. The project includes the construction of new small structures with minor modifications to the landscape.

Sustainability: The Southside Park Picnic Area Renovation project has been reviewed for consistency with the goals, policies, and targets of the City’s Sustainability Master Plan (SMP), the Parks and Recreation Sustainability Plan (PRSP), and the 2030 General Plan. The renovation of this park will advance these plans’ goals, policies and targets by reducing water consumption and expanding recreation opportunities. The park development will be consistent with sustainable design and development standards now applied to City park design to incorporate site furniture manufactured from recycled materials and a water efficient centralized irrigation system. This project is using recycled content material as follows: concrete pavement (13.5%).

Committee/Commission Action: Not applicable.

Rationale for Recommendation: The formal bidding process for the Southside Park Picnic Area Renovation project was posted in accordance with City Code 3.60 and Administrative Policy Instruction #4002. The project was posted and the bids were opened on July 27, 2011. The staff/engineer’s estimate for the project was \$255,695 (base bid plus three additive alternates). Staff received seven bids and the results are listed below.

NO.	<u>CONTRACTOR</u>	<u>BASE BID</u>	<u>ADDITIVE ALTERNATES</u>	<u>TOTAL BID</u>
1	RSC General & Engineering, Inc.	\$175,828.37	\$29,473.08	\$205,301.45
2	JM Slover	\$180,155.00	\$32,605.00	\$212,760.00
3	Parker Landscape Development	\$182,554.00	\$30,255.00	\$212,809.00
4	Sierra Valley Construction	\$186,979.00	\$46,769.00	\$233,748.00
5	Grand Sierra Construction	\$211,064.00	\$30,410.00	\$241,474.00
6	Environmental Landscape Solutions (ELS)	\$208,115.00	\$37,300.00	\$245,415.00
7	Hemington Landscape Services	\$238,548.00	\$37,804.00	\$276,352.00

The project award will be for the base bid and two additive alternates (security cameras) in an amount not to exceed \$196,186.37. The group picnic area being renovated is located in the northwest corner of Southside Park at T and 6th Streets. The improvements to the park consist of the renovation of 0.57-acres including: clearing and grubbing, demolition, grading, a low water efficient landscaping and irrigation system modifications, accessible concrete flatwork, concrete mowstrips, picnic tables, game tables, serving tables, group barbeque grills, drinking fountain, trash receptacles, signage, and security cameras. Pursuant to City Code Section 3.60.020, it was determined that RSC General & Engineering, Inc. had the lowest, responsive total bid. Construction is expected to begin in September 2011 and be complete by fall 2011.

Financial Considerations: Funding for this project is from Park Development Impact Fees (PIF), Fund 3204, in the amount of \$142,985, and Capital Grants (LWCF Grant), Fund 3704, in the amount of \$142,985. Staff is requesting City Council approval to appropriate an additional \$24,000 from Park Development Impact Fees (PIF), Fund 3204, to L19162104, to award two additive alternates for two security cameras. Ongoing maintenance is approved in the existing Department operating budget.

Emerging Small Business Development (ESBD): The project is funded with Land and Water Conservation (LWCF) dollars, a federal funding source, and Minority and Women Owned Business Enterprise (M/WBE) Good Faith Effort subcontracting efforts and Davis-Bacon federal wage determinations apply. Emerging and Small Business Enterprise (E/SBE) requirements are held in abeyance when M/WBE requirements apply for federally funded contracts.


Background

Southside Park is an existing 19.5-acre community park located at 2115 6th Street in the Central City Community Plan Area (PA1).

On April 3, 2007, City Council adopted Resolution No. 2007-187 supporting the development of a Land and Water Conservation Fund (LWCF) Grant application for the renovation of the group picnic area at Southside Park. On May 19, 2009, City Council adopted Resolution 2009-301 establishing the Capital Improvement Program (CIP) for the Southside Park Picnic Area Renovation project (L19162104) and appropriating LWCF grant funds in the amount of \$142,985 and the required local matching funds in the amount of \$142,985 from Park Development Impact Fees (PIF), Fund 3204, to the project.

On June 8, 2011, the improvements for the Southside Park Picnic Area were reviewed and supported by the Southside Park Neighborhood Association.

The Southside Park Picnic Area project consists of the renovation of 0.57-acres including: clearing and grubbing, demolition, grading, a low water efficient landscaping and irrigation system modifications, accessible concrete flatwork, concrete mowstrips, picnic tables, game tables, serving tables, group barbeque grills, drinking fountain, trash receptacles, signage, and security cameras. Construction is expected to begin in September 2011 and be complete by late fall 2011.

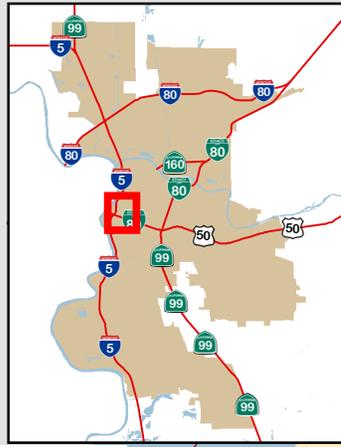


[Back to Table of Contents](#)



Southside Park Picnic Area Renovation


Southside Park

-  Southside Park
-  City Limits



City of Sacramento
Department of Parks and Recreation
Southside Park

SOUTHSIDE PARK PICNIC AREA IMPROVEMENTS

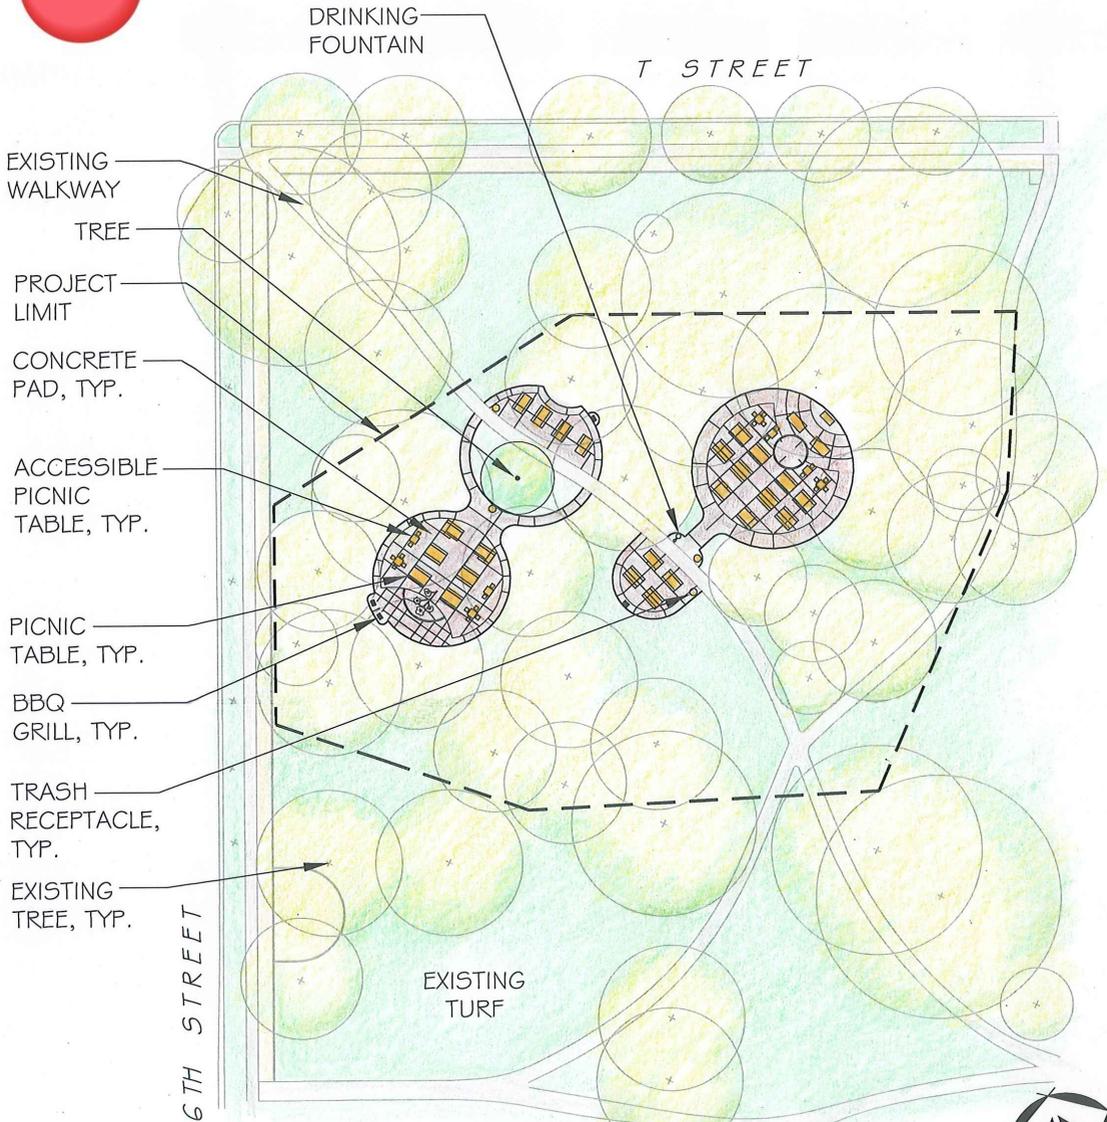



RESOLUTION NO. 2011-

Adopted by the Sacramento City Council

August 30, 2011

AWARDING CONTRACT FOR SOUTHSIDE PARK PICNIC AREA RENOVATION PROJECT (L19162104) TO RSC GENERAL & ENGINEERING, INC.

BACKGROUND

- A. Southside Park is an existing 19.5-acre community park located at 2115 6th Street in Central City Community Plan Area (PA1).
- B. The Southside Park Neighborhood Association supported the Southside Park Picnic Area improvements on June 8, 2011.
- C. On April 3, 2007, City Council adopted Resolution No. 2007-187 supporting the development of a Land and Water Conservation Fund (LWCF) Grant application for the renovation of the group picnic area at Southside Park, which was subsequently awarded.
- D. On May 19, 2009, City Council adopted Resolution 2009-301 establishing the Capital Improvement Program (CIP) for the Southside Park Picnic Area Renovation project (L19162104) and appropriating LWCF grant funds in the amount of \$142,985 and the required local matching funds in the amount of \$142,985 from Park Development Impact Fees (PIF), Fund 3204, to the project.
- E. City Code Chapter 3.60 identifies the general guidelines for contracts for public projects and procedures for bidding and issuing contracts over \$100,000.
- F. The formal bidding process for the Southside Park Picnic Area Renovation project has been completed based on the plans and specifications.
- G. The project award will be for the base bid and two additive alternates (1 & 2).
- H. Staff is requesting City Council approval to appropriate an additional \$24,000 of Community Plan Area 1 Park Development Impact Fees (PIF), Fund 3204, to L19162104 to award two additive alternates.

- I. Pursuant to City Code Section 3.60.020, it was determined that RSC General & Engineering, Inc. was the lowest responsive bidder with a total bid price of \$175,828.37 for the base bid and with additive alternates 1 & 2, the total amount proposed for the contract award is \$196,186.37.

BASED ON THE FACTS SET FORTH IN THE BACKGROUND, THE CITY COUNCIL RESOLVES AS FOLLOWS:

- Section 1. The contract plans and specifications for the Southside Park Picnic Area Renovation project (L19162104) are approved.
- Section 2. That \$24,000 of Park Development Impact Fees, Fund 3204, is appropriated to L19162104.
- Section 3. The contract for the Southside Park Picnic Area Renovation project is awarded to RSC General & Engineering, Inc. for an amount not to exceed \$196,186.37.
- Section 3. The City Manager, or City Manager's designee, is authorized to execute the contract with RSC General & Engineering, Inc. for the Southside Park Picnic Area Renovation project attached as Exhibit A.

Table of Contents:

Exhibit A: Contract for the Southside Park Picnic Area Renovation



AGREEMENT
(Construction Contract Over \$25,000)

THIS AGREEMENT, dated for identification August 30, 2011, is made and entered into between the CITY OF SACRAMENTO, a municipal corporation (“City”), and RSC GENERAL & ENGINEERING, INC., 7475 14TH AVENUE, SACRAMENTO, CA 95820 (“Contractor”), in the amount of: ONE HUNDRED NINETY SIX THOUSAND ONE HUNDRED EIGHTY SIX DOLLARS AND THIRTY SEVEN CENTS (\$196,186.37).

The City and Contractor hereby mutually agree as follows:

1. CONTRACT DOCUMENTS

The Contract Documents, sometimes also referred to as the “Contract,” consist of the following items, which are hereby incorporated by reference as if set forth in full in this Agreement:

- The Notice to Contractors
- The Proposal Form submitted by the Contractor
- The Instructions to Bidders
- The Emerging and Small Business Enterprise (ESBE) Requirements
- The Requirements for the Non-Discrimination in Employee Benefits by City Contractors Ordinance and the Declaration of Compliance
- The City’s Reference Guide for Construction Contracts
- The Addenda, if any
- This Agreement
- The Standard Specifications
- The Special Provisions
- The Plans and Technical Specifications
- The drawings and other data and all developments thereof prepared by City pursuant to the Contract
- Any modifications of any of the foregoing made or approved by City, including but not limited to duly authorized change orders.

Unless specifically noted otherwise, references to the “Standard Specifications” shall mean and refer to the Standard Specifications for Public Construction of the City of Sacramento approved by the Sacramento City Council on June 4, 2007 (Resolution No. 2007-350), and any subsequent amendments thereto approved by the Sacramento City Council or the Sacramento City Manager. Work called for in any one Contract Document and not mentioned in another is to be performed and executed as if mentioned in all Contract Documents. The table of contents, titles and headings contained in the Contract Documents are provided solely to facilitate reference to various provisions of the Contract Documents and in no way affect or limit the interpretation of the provisions to which they refer.

2. DEFINITIONS

Unless otherwise specifically provided herein, all words and phrases defined in the Standard Specifications shall have the same meaning and intent in this Agreement.

3. AGREEMENT CONTROLS

In the event of a conflict between any of the terms and conditions set forth in this Agreement and the terms and conditions set forth in other Contract Documents, the terms and conditions set forth in this Agreement shall prevail, except that the provisions of any duly authorized change order shall prevail over any conflicting provisions of this Agreement.

4. SCOPE OF CONTRACT

Contractor agrees to furnish all tools, equipment, apparatus, facilities, labor, material and transportation necessary to perform and complete in a good and workmanlike manner to the satisfaction of City, all the Work called for in the Contract Documents entitled:

SOUTHSIDE PARK PICNIC AREA (L19162104)

including the Work called for in the following alternative bid items described in the Proposal Form:

ADDITIVE ALTERNATES 1&2

Contractor agrees to perform such Work in the manner designated in and in strict conformity with the Contract Documents.

5. CONTRACT AMOUNT AND PAYMENTS

City agrees to pay and Contractor agrees to accept, as complete payment for the above Work, in accordance with the schedule and procedures set forth in the Contract Documents and subject to deductions, withholdings and additions as specified in the Contract Documents, a total sum that shall not exceed the total bid amount set forth in Contractor's Proposal Form. In addition, subject to deductions, withholdings and additions as specified in the Contract Documents, payment for individual items of the Work shall be computed as follows:

(A) For items of the Work for which a lump sum price is specified in Contractor's Proposal Form, Contractor shall be paid the lump sum price(s) specified in Contractor's Proposal Form; and

(B) For items of the Work for which a unit price is specified in Contractor's Proposal Form, Contractor shall be paid the sum computed at such unit price, or computed at a different price if such different price is determined by City in accordance with the Standard Specifications, based on the actual amount of each such item performed and/or furnished and incorporated in the Work; provided that in no event shall the total sum for a unit price item exceed the total bid amount set forth for such item in the Contractor's Proposal Form, unless authorized by Change Order.

6. PROGRESS PAYMENTS

Subject to the terms and conditions of the Contract, City shall cause payments to be made upon demand of Contractor as follows:

(A) On or about the first of the month, the Engineer shall present to the Contractor a statement showing the amount of labor and materials incorporated in the Work through the twentieth (20) calendar day of the preceding month. After both Contractor and Engineer approve the statement in writing, and the City's labor compliance officer provides written approval, the City shall issue a certificate for ninety (90) percent of the amount it shall find to be due, subject

to any deductions or withholdings authorized or required under the Contract or any applicable Laws or Regulations.

(B) No inaccuracy or error in said monthly estimates shall operate to release Contractor from damages arising from such Work or from enforcement of each and every provision of the Contract Documents, and City shall have the right subsequently to correct any error made in any estimate for payment.

(C) Contractor shall not be paid for any defective or improper Work.

(D) The remaining ten (10) percent of the value of the Work performed under the Contract, if unencumbered and subject to any deductions or withholdings authorized or required under the Contract or any applicable Laws or Regulations, shall be due and payable beginning thirty-five (35) days after completion and final acceptance of the Work by City; provided that the City may determine, in its sole discretion, to release up to fifty (50) % of such retention, in whole or in part, at any time. Acceptance by Contractor of the final payment shall constitute a waiver of all claims against the City arising under the Contract Documents, except for disputed claims in stated amounts that the Contractor specifically reserves in writing, but only to the extent that the Contractor has complied with all procedures and requirements applicable to the presentation and processing of such claim(s) under the Contract Documents. Contractor shall be entitled to substitute securities for retention or to direct that payments of retention be made into escrow, as provided in Public Contract Code Section 22300, upon execution of the City's Escrow Agreement for Security Deposits in Lieu of Retention.

(E) The parties agree that, for purposes of the timely progress payment requirements specified in Public Contract Code Section 20104.50, the date that the City receives a statement jointly approved by the Contractor and the Engineer as provided above shall be deemed to constitute the date that City receives an undisputed and properly submitted payment request from the Contractor. Progress payments not made within 30 days after this date may be subject to payment of interest as provided in Section 20104.50.

(F) An updated progress schedule to be accepted by the project manager shall accompany every pay request.

7. RETENTION OF SUMS CHARGED AGAINST CONTRACTOR

When, under the provisions of this Contract or any applicable Laws or Regulations, City is authorized or required to withhold, deduct or charge any sum of money against Contractor, City may deduct and retain the amount of such charge from the amount of the next succeeding progress estimate(s), or from any other moneys due or that may become due Contractor from City. If, on completion or termination of the Contract, sums due Contractor are insufficient to pay City's charges, City shall have the right to recover the balance from Contractor or its Sureties.

8. COMMENCEMENT AND PROSECUTION OF WORK

Contractor shall commence the Work not later than fifteen (15) working days after the date of the written Notice to Proceed from City to Contractor and shall diligently prosecute the Work to final completion. The phrase "commence the Work" means to engage in a continuous program on-site including, but not limited to, site clearance, grading, dredging, land filling and the fabrications, erection, or installation of the Work. The Notice to Proceed shall be issued within fifteen (15)

calendar days following execution of the Agreement by the City and the filing by Contractor of the required Bonds and proof of insurance, provided that the Engineer may delay issuance of the Notice to Proceed if the Engineer determines in the Engineer's sole discretion that conditions on the site of the Work are unsuitable for commencement of the Work. After the Notice to Proceed is issued, the continuous prosecution of Work by Contractor shall be subject only to Excusable Delays as defined in this Agreement.

9. TIME OF COMPLETION

The entire Work shall be brought to completion in the manner provided for in the Contract Documents on or before Forty (40) Working days from the date of the Notice to Proceed (hereinafter called the "Completion Date") unless extensions of time are granted in accordance with the Contract Documents.

Failure to complete the entire Work by the Completion Date and in the manner provided for in the Contract Documents shall subject Contractor to liquidated damages as provided in this Agreement. Time is and shall be of the essence in the performance of the Contract and the Work.

10. PAYMENTS DO NOT IMPLY ACCEPTANCE OF WORK

The payment of any progress payment, or the acceptance thereof by Contractor, shall not constitute acceptance of the Work or any portion thereof and shall in no way reduce the liability of Contractor to replace unsatisfactory work or material, whether or not the unsatisfactory character of such work or material was apparent or detected at the time such payment was made.

11. ACCEPTANCE NOT RELEASE

Contractor shall correct immediately any defective or imperfect work or materials that may be discovered before final acceptance of the entire Work, whether or not such defect or imperfection was previously noticed or identified by the City. The inspection of the Work, or any part thereof, shall not relieve Contractor of any of its obligations to perform satisfactory work as herein specified.

Failure or neglect on the part of City or any of its officers, employees or authorized agents to discover, identify, condemn or reject defective or imperfect work or materials shall not be construed to imply an acceptance of such work or materials, if such defect or imperfection becomes evident at any time prior to final acceptance of the entire Work, nor shall such failure or neglect be construed as barring City from enforcing Contractor's warranty(ies) or otherwise recovering damages or such a sum of money as may be required to repair or rebuild the defective or imperfect work or materials whenever City may discover the same, subject only to any statutes of limitation that may apply to any such claim.

12. CITY'S RIGHT TO TAKE POSSESSION OF THE WORK IN WHOLE OR IN PART

The City shall have the right at any time to enter upon the Work and perform work not covered by this Contract, or to occupy and use a portion of the Work, prior to the date of the final acceptance of the Work as a whole, without in any way relieving Contractor of any obligations under this Contract.

13. NO WAIVER OF REMEDIES

Neither the inspection by City, its officers, employees or agents, nor any certificate or other approval for the payment of money, nor any payment for, nor acceptance of the whole or any part of the Work by City, nor any extensions of time, nor any position taken by City, its officers, employees or its agents shall operate as a waiver of any provision of the Contract Documents nor of any power herein reserved to City or any right to damages herein provided, nor shall any waiver of any breach of this Agreement be held to be a waiver of any other or subsequent breach. All remedies provided in the Contract Documents shall be taken and construed as cumulative; in addition to each and every other remedy herein provided, the City shall have any and all equitable and legal remedies that it would in any case have.

14. WARRANTY

Except as otherwise expressly provided in the Contract Documents, and excepting only items of routine maintenance, ordinary wear and tear and unusual abuse or neglect by City, Contractor warrants and guarantees all Work executed and all supplies, materials and devices of whatsoever nature incorporated in or attached to the Work, or otherwise provided as a part of the Work pursuant to the Contract, to be absolutely free of all defects of workmanship and materials for a period of one year after final acceptance of the entire Work by the City. Contractor shall repair or replace all work or material, together with any other work or material that may be displaced or damaged in so doing, that may prove defective in workmanship or material within this one year warranty period without expense or charge of any nature whatsoever to City.

In the event that Contractor shall fail to comply with the conditions of the foregoing warranty within ten (10) days after being notified of the defect in writing, City shall have the right, but shall not be obligated, to repair, or obtain the repair of, the defect and Contractor shall pay to City on demand all costs and expense of such repair. Notwithstanding anything herein to the contrary, in the event that any defect in workmanship or material covered by the foregoing warranty results in a condition that constitutes an immediate hazard to public health or safety, or any property interest, or any person, City shall have the right to immediately repair, or cause to be repaired, such defect, and Contractor shall pay to City on demand all costs and expense of such repair. The foregoing statement relating to hazards to health, safety or property shall be deemed to include both temporary and permanent repairs that may be required as determined in the sole discretion and judgment of City.

In addition to the above, the Contractor shall make a written assignment of all manufacturer's and other product warranties to the City, prior to completion and final acceptance of the Work by City.

The Contractor's Performance Bond shall secure the performance of the Contractor's obligations under this Section 14, and the Contractor and its Surety shall be jointly and severally liable for these obligations.

15. LIQUIDATED DAMAGES IF WORK NOT COMPLETED ON TIME

(A) The actual fact of the occurrence of damages and the actual amount of the damages that City would suffer if the entire Work, and/or any specified portion thereof, were not completed within the time(s) specified herein are dependent upon many circumstances and conditions that could prevail in various combinations, and for this reason, it is impracticable and extremely difficult to fix the actual damages. Damages that City would suffer in the event of such delay include: loss of the use of the project; expenses of prolonged assignment to the project of an

architectural and/or engineering staff; prolonged costs of administration, inspection, and supervision; increased operational expenses and/or impaired operation of other facilities dependent upon completion of the project; and the loss and inconvenience suffered by the public within the City of Sacramento by reason of the delay in the completion of the project or portion thereof. Accordingly, the parties agree, and by execution of this Agreement, Contractor acknowledges that it understands and agrees, that the amount(s) set forth herein as liquidated damages reflect the parties' best efforts at the time of entering into the Contract to estimate the damages that may be incurred by City and the public due to the Contractor's delay in completion of the Work and/or any specified portion thereof, and shall be presumed to be the amount of damages sustained by the failure of Contractor to complete the entire Work and/or any specified portion thereof within the time(s) specified herein.

(B) Contractor shall pay liquidated damages to City for failure to complete the entire Work by the Completion Date (as extended in accordance with the Contract Documents, if applicable) in the amount of One Thousand Dollars (\$1,000.00) for each calendar day after the Completion Date (as extended in accordance with the Contract Documents, if applicable), continuing to the time at which the entire Work is completed. Such amount is the actual cash value agreed upon by the City and Contractor as the loss to City and the public resulting from Contractor's default.

The parties agree, and by execution of this Agreement, Contractor acknowledges that it understands and agrees, that the foregoing provisions provide for the imposition of liquidated damages from the Completion Date (as extended in accordance with the Contract Documents, if applicable) until the date of completion of the entire Work as determined by the Engineer in accordance with Section 8-4 of the Standard Specifications, whether or not the Work or any portion thereof is claimed or determined to be substantially complete prior to such date of completion.

THE FOLLOWING ADDITIONAL LIQUIDATED DAMAGES PROVISION(S) APPLY IF CHECKED:

In addition to the liquidated damages specified above, Contractor shall pay additional liquidated damages to City for failure to complete the portion of the Work specified below by the milestone date specified below (as such milestone date may be extended in accordance with the Contract Documents, if applicable). The amount of such additional liquidated damages shall be either *[check one]*:

a lump sum amount of _____, OR

the daily amount of _____ for each calendar day after such milestone date (as extended in accordance with the Contract Documents, if applicable), continuing to the time at which such portion of the Work is completed.

Such amount is the actual cash value agreed upon by the City and Contractor as the additional loss to City and the public resulting from Contractor's default.

Portion of the Work

Milestone Date

CONTRACTOR'S ACKNOWLEDGMENT: _____

In addition to the potential damages described above, failure to complete the entire Work within the time(s) specified herein may expose the City to penalties or fines and/or may negatively affect the availability of project funding. In recognition of these potential damages, in addition to the liquidated damages specified above, Contractor shall pay additional liquidated damages to City in the lump sum amount of _____ if the entire Work is not completed by _____. Such amount is the actual cash value agreed upon by the City and Contractor as the additional loss to City and the public resulting from Contractor's default.

CONTRACTOR'S ACKNOWLEDGMENT: _____

(C) In the event Contractor shall become liable for liquidated damages, City, in addition to all other remedies provided by law, shall have the right to withhold any and all payments that otherwise would be or become due Contractor until the liability of Contractor under this section is finally determined. City shall have the right to use and apply such payments, in whole or in part, to reimburse City for all liquidated damages due or to become due to City. Any remaining balance of such payments shall be paid to Contractor only after discharge in full of all liability incurred by Contractor under this section or otherwise under any provision of the Contract Documents or any applicable Law or Regulation. If the sum so retained by City is not sufficient to discharge all such liabilities of Contractor, Contractor shall continue to remain liable to City until all such liabilities are satisfied in full. No failure by City to withhold any payment as specified above shall in any manner be construed to constitute a release of any such liabilities nor a waiver of the City's right to withhold payment for such liabilities.

16. INDEMNITY AND HOLD HARMLESS

(A) Contractor shall defend, hold harmless and indemnify the City, its officers, employees, and agents, and each and every one of them, from and against any and all actions, damages, costs, liabilities, claims, demands, losses, judgments, penalties, costs and expenses of every type and description, whether arising on or off the site of the Work, including, but not limited to, any fees and/or costs reasonably incurred by City's staff attorneys or outside attorneys and any fees and expenses incurred in enforcing this provision (hereafter collectively referred to as "Liabilities"), including but not limited to Liabilities arising from personal injury or death, damage to personal, real or intellectual property or the environment, contractual or other economic damages, or regulatory penalties, arising out of or in any way connected with performance of or failure to perform the Work by the Contractor, any subcontractor or agent, anyone directly or indirectly employed by any of them or anyone for whose acts any of them may be liable, whether or not (i) such Liabilities are caused in part by a party indemnified hereunder, or (ii) such Liabilities are litigated, settled or reduced to judgment; provided that the foregoing indemnity does not apply to liability for damages for death or bodily injury to persons, injury to property, or other loss, damage or expense to the extent arising from (i) the sole negligence or willful misconduct of, or defects in design furnished by, City, its agents, servants, or independent contractors who are directly responsible to City, or (ii) the active negligence of City.

(B) The existence or acceptance by City of any of the insurance policies or coverages described in this Agreement shall not affect or limit any of City's rights under this Section 16, nor shall the limits of such insurance limit the liability of Contractor hereunder. The provisions of this Section 16 shall survive any expiration or termination of the Contract.

17. CONTRACTOR SHALL ASSUME RISKS

Until the completion and final acceptance by City of all Work under this Contract, the Work shall be under Contractor's responsible care and charge, and Contractor, at no cost to City, shall rebuild, repair, restore and make good all injuries, damages, re-erections, and repairs occasioned or rendered necessary by accidental causes of any nature, to all or any portions of the Work.

18. GENERAL LIABILITY OF CONTRACTOR

Except as otherwise herein expressly stipulated, Contractor shall perform all the Work and furnish all the labor, materials, tools, equipment, apparatus, facilities, transportation, power and light, and appliances, necessary or proper for performing and completing the Work herein required in the manner and within the time herein specified. The mention of any specific duty or liability of Contractor shall not be construed as a limitation or restriction of any general liability or duty of Contractor, and any reference to any specific duty or liability shall be construed to be solely for the purpose of explanation.

19. INSURANCE

During the entire term of this Contract and until completion and final acceptance of the Work as provided in the Contract Documents, Contractor shall maintain in full force and effect the insurance coverage described in this section.

Full compensation for all premiums that Contractor is required to pay for the insurance coverage described herein shall be included in the compensation specified for performance of the Work under the Contract. No additional compensation will be provided for Contractor's insurance premiums.

It is understood and agreed by the Contractor that its liability to the City shall not in any way be limited to or affected by the amount of insurance coverage required of or carried by the Contractor.

(A) **Minimum Scope and Limits of Insurance Coverage**

- (1) **Commercial General Liability Insurance**, providing coverage at least as broad as ISO CGL Form 00 01 on an occurrence basis for bodily injury, including death, of one or more persons, property damage and personal injury, with limits of not less than one million dollars (\$1,000,000) per occurrence. The policy shall provide contractual liability and products and completed operations coverage for the term of the policy.
- (2) **Automobile Liability Insurance** providing coverage at least as broad as ISO Form CA 00 01 on an occurrence basis for bodily injury, including death, of one or more persons, property damage and personal injury, with limits of not less than one million dollars (\$1,000,000) per occurrence. The policy shall provide coverage for owned, non-owned and/or hired autos as appropriate to the operations of the Contractor.

- (3) **Workers' Compensation Insurance** with statutory limits, and **Employers' Liability Insurance** with limits of not less than one million dollars (\$1,000,000). The Worker's Compensation policy shall include a waiver of subrogation.

(B) **Additional Insured Coverage**

- (1) **Commercial General Liability Insurance**: The City, its officials, employees and volunteers shall be covered by policy terms or endorsement as additional insureds as respects general liability arising out of activities performed by or on behalf of Contractor, products and completed operations of Contractor, and premises owned, leased or used by Contractor. The general liability additional insured endorsement must be signed by an authorized representative of the insurance carrier.

If the policy includes a blanket additional insured endorsement or contractual additional insured coverage, the above signature requirement may be fulfilled by submitting that document with a signed declaration page referencing the blanket endorsement or policy form.

- (2) **Automobile Liability Insurance**: The City, its officials, employees and volunteers shall be covered by policy terms or endorsement as additional insureds as respects auto liability.

(C) **Other Insurance Provisions**

The policies are to contain, or be endorsed to contain, the following provisions:

- (1) Contractor's insurance coverage shall be primary insurance as respects City, its officials, employees and volunteers. Any insurance or self-insurance maintained by City, its officials, employees or volunteers shall be in excess of Contractor's insurance and shall not contribute with it.
- (2) Any failure to comply with reporting provisions of the policies shall not affect coverage provided to City, its officials, employees or volunteers.
- (3) Coverage shall state that Contractor's insurance shall apply separately to each insured against whom claim is made or suit is brought, except with respect to the limits of the insurer's liability.
- (4) City will be provided with thirty (30) days written notice of cancellation or material change in the policy language or terms.

(D) **Acceptability of Insurance**

Insurance shall be placed with insurers with a Bests' rating of not less than A:V. Self-insured retentions, policy terms or other variations that do not comply with the requirements of this Section 19 must be declared to and approved by the City Risk Management Division in writing prior to execution of this Agreement.

(E) **Verification of Coverage**

(1) Contractor shall furnish City with certificates and required endorsements evidencing the insurance required. Contractor shall provide initial insurance documents to the Engineer upon request, prior to execution of the final contract. All future insurance renewal documents shall be sent to:

EBIX BPO
212 Kent Street
Portland, MI, 48875
Phone: (517) 647-1700
Fax: (517) 647-7900
Email: CertsOnly@periculum.com

Copies of policies shall be delivered to the City on demand. Certificates of insurance shall be signed by an authorized representative of the insurance carrier.

(2) The City may withdraw its offer of contract or cancel the Contract if the certificates of insurance and endorsements required have not been provided prior to execution of this Agreement. The City may withhold payments to Contractor and/or cancel the Contract if the insurance is canceled or Contractor otherwise ceases to be insured as required herein.

(F) Subcontractors

Contractor shall require and verify that all subcontractors maintain insurance coverage that meets the minimum scope and limits of insurance coverage specified in subsection A, above.

20. FAILURE TO MAINTAIN BONDS OR INSURANCE

If, at any time during the performance of this Contract, Contractor fails to maintain any item of the bonds and/or insurance required under the Contract in full force and effect, Contractor shall immediately suspend all work under the Contract and notify City in writing of such failure. After such notice is provided, or if City discovers such failure and notifies Contractor, the City thereafter may withhold all Contract payments due or that become due until notice is received by City that such bonds and/or insurance have been restored in full force and effect and that the premiums therefore have been paid for a period satisfactory to the Division of Risk Management. Contractor shall not resume work until notified by City to do so, and the City shall have no responsibility or liability for any costs incurred by Contractor as a result of such suspension of Work.

In addition to the foregoing, any failure to maintain any item of the required bonds and/or insurance at any time during the performance of this Contract will be sufficient cause for termination of the Contract by City.

The Contractor shall be solely responsible for, and shall defend, indemnify and hold harmless the City, its officers, employees and agents against and from, any and all damages, claims, losses, actions, costs or other expenses of any kind incurred by any party as a direct or indirect result of any suspension of Work or termination of the Contract under the provisions of this Section.

21. EXCUSABLE DELAYS

For the purpose of these Contract Documents, the term "Excusable Delay" shall mean, and is limited to, delay caused directly by: acts of God; acts of a public enemy; fires; inclement weather as determined by the Engineer; riots; insurrections; epidemics; quarantine restrictions; strikes; lockouts; sitdowns; acts of a governmental agency; priorities or privileges established for the manufacture, assemble, or allotment of materials necessary in the Work by order, decree or otherwise of the United States or by any department, bureau, commission, committee, agent, or administrator of any legally constituted public authority; changes in the Work ordered by City insofar as they necessarily require additional time in which to complete the Work; the prevention of Contractor from commencing or prosecuting the Work because of the acts of others, excepting Contractor's subcontractors or suppliers; or the prevention of Contractor from commencing or prosecuting the Work because of a Citywide failure of public utility service.

The term "Excusable Delay" shall specifically not include: (i) any delay that could have been avoided by the exercise of care, prudence, foresight and diligence on the part of Contractor; (ii) any delay in the prosecution of any part of the Work that does not constitute a Controlling Operation, whether or not such delay is unavoidable; (iii) any reasonable delay resulting from time required by City for review of any Contractor submittals and for the making of surveys, measurements and inspection; and, (iv) any delay arising from an interruption in the prosecution of the Work on account of reasonable interference by other Contractors employed by City that does not necessarily prevent the completion of the entire Work within the time specified. Excusable Delays, if any, shall operate only to extend the Completion Date (not in excess of the period of such delay as determined by City) and shall not under any circumstances increase the amount City is required to pay Contractor except as otherwise provided in these Contract Documents.

22. CONTRACTOR TO SERVE NOTICE OF DELAYS

Whenever Contractor foresees any delay in the prosecution of the Work, and in any event as soon as possible (not to exceed a period of ten (10) calendar days) after the initial occurrence of any delay that Contractor regards as or may later claim to be an Excusable Delay, the Contractor shall notify the Engineer in writing of such delay and its cause, in order that the Engineer: (i) may take immediate steps to prevent if possible the occurrence or continuance of the delay; or (ii) if this cannot be done, may determine whether the delay is to be considered excusable, how long it continues, and to what extent the prosecution and completion of the Work are delayed thereby. Said written notice shall constitute an application for an extension of time only if the notice requests such an extension and sets forth the Contractor's estimate of the additional time required together with a full description of the cause of the delay relied upon.

After the completion of any part or whole of the Work, the Engineer, in estimating the amount due Contractor, will assume that any and all delays that may have occurred in its prosecution and completion were not Excusable Delays, except for such delays for which the Contractor has provided timely written notice as required herein, and that the Engineer has found to be excusable. Contractor shall not be entitled to claim Excusable Delay for any delay for which the Contractor failed to provide such timely written notice.

23. EXTENSION OF TIME

If the Contractor complies with Section 22, above, and the Engineer finds a delay claimed by the Contractor to be an Excusable Delay, the Contractor shall be allowed an extension of time to complete the Work that is proportional to the period of Excusable Delay determined by the Engineer, subject to the approval by City of a change order granting such time extension. During

a duly authorized extension for an Excusable Delay, City shall not charge liquidated damages against the Contractor for such delay.

If the City extends the time to complete the Work as provided herein, such extension shall in no way release any warranty or guarantee given by Contractor pursuant to the provisions of the Contract Documents, nor shall such extension of time relieve or release the sureties of the Bonds provided pursuant to the Contract Documents. By executing such Bonds, the Sureties shall be deemed to have expressly agreed to any such extension of time. The granting of any extension of time as provided herein shall in no way operate as a waiver on the part of City of its rights under this Contract, excepting only extension of the Completion Date for such period of Excusable Delay as may be determined by the Engineer and approved by a duly authorized change order.

24. NO PAYMENT FOR DELAYS

No damages or compensation of any kind shall be paid to Contractor or any subcontractor because of delays in the progress of the Work whether or not such delays qualify for extension of time under this Agreement; except that this provision shall not preclude the recovery of damages for a delay caused by the City that is unreasonable under the circumstances and that is not within the contemplation of the parties, provided that the Contractor timely submits all such written notice(s) and fully complies with such other procedures as may be specified in the Contract Documents or any Laws or Regulations for Contractor to claim damages for such delay.

25. CHANGES IN THE WORK

Changes in the Work authorized or directed in accordance with the Contract Documents and extensions of time of completion made necessary by reason thereof shall not in any way release any warranty or guarantee given by Contractor pursuant to the provisions of the Contract Documents, nor shall such changes in the Work relieve or release the Sureties on Bonds provided pursuant to the Contract Documents. By executing such Bonds, the Sureties shall be deemed to have expressly agreed to any such change in Work and to any extension of time made by reason thereof.

26. TERMINATION AFTER COMPLETION DATE

In addition to any other rights City may have, if any services or work required under the Contract (including but not limited to punch list items) are not completed as of the Completion Date (as adjusted by any extensions of time for Excusable Delays granted pursuant to the Contract Documents), City may terminate the Contract at any time after the Completion Date (as adjusted by any extensions of time for Excusable Delays granted pursuant to the Contract Documents), by providing a written notice to Contractor specifying the date of termination. Such notice also may specify conditions or requirements that Contractor must meet to avoid termination of the Contract on such date. If Contractor fails to fulfill all such conditions and requirements by such termination date, or, if no such conditions or requirements are specified, Contractor shall cease rendering services and performing work on such termination date, and shall not be entitled to receive any compensation for services rendered or work performed after such termination date. In the event of such termination, Contractor shall remain liable to City for liquidated damages incurred for any period of time prior to the termination date.

In addition to any other charges, withholdings or deductions authorized under the Contract or any Laws or Regulations, if City terminates the Contract pursuant to this section, City may withhold and deduct from any payment and/or retention funds otherwise due Contractor any sum necessary

to pay the City's cost of completing or correcting, or contracting for the completion or correction of, any services or work under the Contract that are not completed to the satisfaction of the City or that otherwise are deficient or require correction as of such termination date, including but not limited to incomplete punch list items. Such costs shall include all of the City's direct and indirect costs incurred to complete or correct such services or work, including the City's administrative and overhead costs. If the amount of payment(s) and/or retention funds otherwise due the Contractor are insufficient to pay such costs, City shall have the right to recover the balance of such costs from the Contractor and/or its Surety(ies).

27. TERMINATION FOR CONVENIENCE

Upon written notice to the Contractor, the City may at any time, without cause and without prejudice to any other right or remedy of the City, elect to terminate the Contract for the convenience of City. In such case, the Contractor shall be paid (without duplication of any items, and after deduction and/or withholding of any amounts authorized to be deducted or withheld by the Contract Documents or any Laws or Regulations):

- (A) For Work executed in accordance with the Contract Documents prior to the effective date of termination and determined to be acceptable by the Engineer, including fair and reasonable sums for overhead and profit on such Work;
- (B) For reasonable claims, costs, losses, and damages incurred in settlement of terminated contracts with subcontractors, suppliers, and others; and
- (C) For reasonable expenses directly attributable to termination.

Contractor shall not be paid for any loss of anticipated profits or revenue for any Work not performed prior to termination, nor for any economic loss arising out of or resulting from such termination, except for the payments listed in this section. Contractor's warranty under Section 14 of this Agreement shall apply, and Contractor shall remain responsible for all obligations related to such warranty, with respect to all portions of the Work performed prior to the effective date of the termination for convenience pursuant to this section. The City shall be entitled to have any or all remaining Work performed by other contractors or by any other means at any time after the effective date of a termination for convenience pursuant to this section.

28. TERMINATION FOR BREACH OF CONTRACT

If Contractor abandons the Work under this Contract, or if the Contract or any portion of the Contract is sublet or assigned without the consent of the City, or if the Engineer determines in the Engineer's sole discretion that the conditions of the Contract in respect to the rate of progress of the Work are not being fulfilled or any part thereof is unnecessarily delayed, or if Contractor violates or breaches, or fails to execute in good faith, any of the terms or conditions of the Contract, or if Contractor refuses or fails to supply enough properly skilled labor or materials or refuses or fails to make prompt payment to subcontractors for material or labor, or if Contractor disregards any Laws or Regulations or proper instruction or orders of the Engineer, then, notwithstanding any provision to the contrary herein, the City may give Contractor and its Sureties written notification to immediately correct the situation or the Contract shall be terminated.

In the event that such notice is given, and, in the event such situation is not corrected, or arrangements for correction satisfactory to the City are not made, within ten (10) calendar days from the date of such notice or within such other period of time as may be specified by the City in the notice, the Contract shall upon the expiration of said period cease and terminate. In the event of any such termination, City may take over the Work and prosecute the Work to completion, or otherwise, and the Contractor and its Sureties shall be liable to City for any cost occasioned City thereby, as hereinafter set forth.

In the event City completes the Work, or causes the Work to be completed, no payment of any kind shall be made to Contractor until the Work is complete. The cost of completing the Work, including but not limited to, extra costs of project administration and management incurred by City, both direct or indirect, shall be deducted from any sum then due, or that becomes due, to Contractor from City. If sums due to Contractor from City are less than the cost of completing the Work, Contractor and its Sureties shall pay City a sum equal to this difference on demand. In the event City completes the Work, and there is a sum remaining due to Contractor after City deducts the costs of completing the Work, then City shall pay such sum to Contractor. The Contractor and Contractor's Sureties shall be jointly and severally liable for all obligations imposed on Contractor hereunder.

No act by City before the Work is finally accepted, including, but not limited to, exercise of other rights under the Contract, actions at law or in equity, extensions of time, payments, assessments of liquidated damages, occupation or acceptance of any part of the Work, waiver of any prior breach of the Contract or failure to take action pursuant to this section upon the happening of any prior default or breach of Contractor, shall be construed to be a waiver or estoppel of the City's right to act pursuant to this Section upon any subsequent event, occurrence or failure by Contractor to fulfill the terms and conditions of the Contract. The rights of City to terminate the Contract pursuant to this Section and pursuant to Sections 26 and 27 are cumulative and are in addition to all other rights of City pursuant to the Contract and at law or in equity.

29. CONTRACTOR BANKRUPT

If Contractor should commence any bankruptcy proceeding, or if Contractor is adjudged a bankrupt, or if Contractor makes any assignment for the benefit of creditors, or if a receiver is appointed on account of Contractor's insolvency, then the City may, without prejudice to any other right or remedy, terminate the Contract and complete the work by giving notice as provided in Section 28 above.

30. SURETIES' OBLIGATIONS UPON TERMINATION

If the City terminates the Contract pursuant to Section 28 or Section 29 above:

(A) The Surety under Contractor's performance bond shall be fully responsible for all of the Contractor's remaining obligations of performance under the Contract as if the Surety were a party to the Contract, including without limitation Contractor's obligations, as provided in the Contract Documents, to complete and provide a one-year warranty of the entire Work, pay liquidated damages and indemnify, defend and hold harmless City, up to the full amount of the performance bond.

(B) The Surety under Contractor's payment bond shall be fully responsible for the performance of all of the Contractor's remaining payment obligations for work, services,

equipment or materials performed or provided in connection with the Work or any portion thereof, up to the full amount of the payment bond.

31. ACCOUNTING RECORDS OF CONTRACTOR

During performance of the Contract and for a period of three (3) years after completing the entire Work, Contractor shall maintain all accounting and financial records related to the Contract and performance of the Work in accordance with generally accepted accounting practices, and shall keep and make such records available for inspection and audit by representatives of the City upon reasonable written notice.

32. USE TAX REQUIREMENTS

- (A) Use Tax Direct Payment Permit For all leases and purchases of materials, equipment, supplies, or other tangible personal property used to perform the Contract and shipped from outside California, the Contractor and any subcontractors leasing or purchasing such materials, equipment, supplies or other tangible personal property shall obtain a Use Tax Direct Payment Permit from the California State Board of Equalization ("SBE") in accordance with the applicable SBE criteria and requirements.
- (B) Sellers Permit For any construction contract and any construction subcontract in the amount of \$5,000,000 or more, Contractor and the subcontractor(s) shall obtain sellers permits from the SBE and shall register the jobsite as the place of business for the purpose of allocating local sales and use tax to the City. Contractor and its subcontractors shall remit the self-accrued use tax to the SBE, and shall provide a copy of each remittance to the City.
- (C) The above provisions shall apply in all instances unless prohibited by the funding source for the Contract.

IN WITNESS WHEREOF, the parties hereto have signed this Agreement on the date set for opposite their names.

CONTRACTOR

Under penalty of perjury, I certify that the taxpayer identification number and all other information provided here are correct.

DATE 8/15/11

BY [Signature]
Print Name Richard Spaddy
Title Pres.

BY [Signature]
Print Name John Spaulding
Title Secretary / CFO

Federal ID# 291957465
State ID# C3273437
1007678

City of Sacramento Business Operation Tax Certificate No. (City will not award contract until Certificate Number is obtained)

Type of Business Entity (check one):
 Individual/Sole Proprietor
 Partnership
 Corporation
 Limited Liability Company
 Other (please specify: _____)

CITY OF SACRAMENTO
a municipal corporation

DATE _____

BY _____
For: _____
William H. Edgar, Interim City Manager

Original Approved As To Form:

City Attorney

Attest:

City Clerk
